





ID	i	% Comp	Task Name	Duration	Start	Finish	Predecess	Qtr 1, 2006		
								Dec	Jan	Feb
1		0%	PHASE 2	1 day?	Thu 1/26/06	Thu 1/26/06				
2		85%	Complete Phase 2 Design Documentation	57 days	Mon 7/24/06	Wed 10/11/06				
3	✓	100%	Phase 2 design - Architecture	10 days	Mon 7/24/06	Fri 8/4/06				
4	✓	100%	Phase 2 design - Agent	36 days	Mon 7/24/06	Tue 9/12/06				
8	☰	0%	Review Data Agent extensibility design changes	0 days	Fri 9/22/06	Fri 9/22/06				
9		6%	Update Manager	21 days	Wed 9/13/06	Wed 10/11/06				
10		10%	Draft Created	10 days	Wed 9/13/06	Tue 10/3/06	7			
11		0%	Review and updates	5 days	Wed 10/4/06	Tue 10/10/06	10			
12		0%	Approved	1 day	Wed 10/11/06	Wed 10/11/06	11			
13		68%	Connector	34 days	Mon 8/7/06	Fri 9/22/06				
17	✓	100%	Phase 2 design - Device Server	31 days	Mon 7/24/06	Tue 9/5/06				
21	✓	100%	Phase 2 design - Database	20 days	Mon 7/24/06	Fri 8/18/06				
25	✓	100%	Phase 2 design - Data Server	21 days	Mon 7/24/06	Mon 8/21/06	3SS			
29	✓	100%	Phase 2 design - GUI (Iterative - built into dev)	0 days	Mon 7/24/06	Mon 7/24/06	3SS			
30										
31		24%	Phase 2 code	271 days?	Thu 1/26/06	Mon 2/19/07				
32		72%	Phase 2 code - Agent	39 days	Mon 8/7/06	Fri 9/29/06				
33	✓	100%	Re-add fabric subagent	11 days	Mon 8/7/06	Mon 8/21/06	5			
34		48%	Remove Qlogic copyright from scanner C code	22 days	Wed 8/23/06	Fri 9/22/06	33FS+1 da			
35		0%	Fabric agent unit test	5 days	Mon 9/25/06	Fri 9/29/06	34			
36	✓	100%	Data subagent extensibility	20 days	Mon 8/21/06	Mon 9/18/06	33			
37		60%	Single connector to route both subagents with SSL	20 days	Wed 9/13/06	Tue 10/10/06	4			
38		0%	Update manager support	20 days	Wed 10/4/06	Tue 10/31/06	10			
39		0%	Modify the subagents to use the connector.	5 days	Wed 11/1/06	Tue 11/7/06	38			
40		9%	Phase 2 code - Device Server	69 days	Fri 9/8/06	Fri 12/15/06				
41		50%	Repackage code and define services	13 days	Wed 9/13/06	Fri 9/29/06				
42	✓	100%	Tape package	3 days	Wed 9/13/06	Fri 9/15/06				
43		60%	Disk package	5 days	Mon 9/18/06	Fri 9/22/06	42			
44		60%	Fabric Package	5 days	Mon 9/18/06	Fri 9/22/06	42			
45		0%	CIM-SMIS Package	5 days	Mon 9/25/06	Fri 9/29/06	43			
46		9%	Aperi Platform	57 days	Wed 9/13/06	Mon 12/4/06				
47		25%	Migrate to OSGi Service based Connector	4 days	Mon 9/18/06	Wed 9/27/06	44			

ID	i	% Comp	Task Name	Duration	Start	Finish	Predecess	Qtr 1, 2006		
								Dec	Jan	Feb
48		0%	Define and implement Discovery Plugin and Extensi	8 days	Thu 9/28/06	Tue 10/10/06	43,44,47			
49		50%	Define and implement Control Plugin and Extension	8 days	Wed 9/13/06	Fri 10/6/06	43,44,45			
50		0%	Define and implement Monitoring Plugin and Extens	8 days	Mon 10/9/06	Wed 10/25/06	43,44,49			
51		0%	Integrate Database Plugin and Extension Points	5 days	Fri 10/13/06	Thu 10/26/06	43,44,48			
52		0%	Define and implement Plugin/Extension Points for c	15 days	Fri 10/27/06	Mon 11/27/06	51			
53		0%	Create Aperi Platform Feature Bundle	5 days	Tue 11/28/06	Mon 12/4/06	52			
54		0%	Disk Application	19 days	Fri 10/27/06	Wed 11/22/06				
55		0%	Extend Discovery Plugin for Disk	3 days	Fri 10/27/06	Tue 10/31/06	48,51			
56		0%	Extend Control Plugin for Disk	3 days	Wed 11/1/06	Fri 11/3/06	49,55			
57		0%	Extend Monitoring Plugin for Disk	3 days	Mon 11/6/06	Wed 11/8/06	50,56			
58		0%	Extend Reporting Plugin for Disk	3 days	Thu 11/9/06	Mon 11/13/06	43,57			
59		0%	Create Disk Application Feature Bundle	5 days	Tue 11/14/06	Wed 11/22/06	58			
60		0%	Fabric Application (based on Disk Application)	15 days	Mon 11/27/06	Fri 12/15/06				
61		0%	Extend Discovery Plugin for Fabric	2 days	Mon 11/27/06	Tue 11/28/06	59			
62		0%	Extend Control Plugin for Fabric	2 days	Wed 11/29/06	Thu 11/30/06	61			
63		0%	Extend Monitoring Plugin for Fabric	2 days	Fri 12/1/06	Mon 12/4/06	62			
64		0%	Extend Reporting Plugin for Fabric	2 days	Mon 12/11/06	Tue 12/12/06	63			
65		0%	Create Fabric Application Feature Bundle 4	3 days	Wed 12/13/06	Fri 12/15/06	64			
66		0%	Tape Application (based on Disk Application)	9 days	Tue 12/5/06	Fri 12/15/06				
67		0%	Extend Discovery Plugin for Tape	1 day	Tue 12/5/06	Tue 12/5/06	48,53			
68		0%	Extend Reporting Plugin for Tape	1 day	Wed 12/6/06	Wed 12/6/06	67			
69		0%	Create Tape Application Feature Bundle	2 days	Thu 12/7/06	Fri 12/8/06	68			
70		0%	SVC specific Disk Application	5 days	Mon 12/11/06	Fri 12/15/06				
71		0%	Extend Disk-Control Plugin for SVC	2 days	Mon 12/11/06	Tue 12/12/06	69			
72		0%	Create SVC-Disk Application Feature Bundle	3 days	Wed 12/13/06	Fri 12/15/06	71			
73		0%	Cleanup/Refactoring	54 days	Fri 9/8/06	Wed 12/6/06	68FF			
74		26%	Phase 2 code - Database	70 days	Mon 8/7/06	Mon 11/13/06				
75		36%	Improve performance of port2port queries	50 days	Mon 8/7/06	Mon 10/16/06	22			
76		0%	Introduce classification into fabric discovery (in-band and	20 days	Tue 10/17/06	Mon 11/13/06	75			
77		48%	Phase 2 code - Data Server	67 days	Wed 8/9/06	Fri 11/10/06				
78		48%	Basic Extensibility	67 days	Wed 8/9/06	Fri 11/10/06				
79		81%	Design Details	24 days	Wed 8/9/06	Tue 9/12/06				



ID		% Comp	Task Name	Duration	Start	Finish	Predecess	Qtr 1, 2006		
								Dec	Jan	Feb
80		100%	Resource attributes	6 days	Thu 8/17/06	Thu 8/24/06	97			
81		100%	Alerts	7 days	Fri 8/25/06	Tue 9/5/06	80			
82		100%	Services	2 days	Wed 8/9/06	Thu 8/10/06	26			
83		25%	Jobs	5 days	Wed 9/6/06	Tue 9/12/06	81			
84		41%	Define Extension Points	43.5 days	Fri 8/11/06	Thu 10/12/06				
85		50%	Resource attributes	5 days	Wed 9/13/06	Thu 9/21/06	83			
86		50%	Alerts	5 days	Mon 10/2/06	Thu 10/12/06	35			
87		100%	Services	2 days	Fri 8/11/06	Mon 8/14/06	82			
88		0%	Jobs	5 days	Fri 9/22/06	Thu 9/28/06	85			
89		58%	Create extensions, define metadata objects	48 days	Tue 8/15/06	Fri 10/20/06				
94		5%	Update code to use above	62 days	Wed 8/16/06	Fri 11/10/06				
99		25%	Phase 2 Code - GUI	160 days	Wed 7/5/06	Mon 2/19/07				
100		0%	Legacy GUI Maintenance	142 days	Wed 7/5/06	Wed 1/24/07				
101		50%	New GUI Architecture HLDD	42 days	Wed 7/5/06	Thu 9/14/06	100SS			
102		58%	New GUI Framework and Extensibility	87 days	Wed 7/5/06	Fri 11/3/06				
103		100%	Basic POC: RCP w/legacy backend and encapsu	20 days	Wed 7/5/06	Tue 8/1/06				
108		77%	Plugin Structure, Integration, Error Log	42 days	Wed 8/2/06	Fri 9/29/06				
109		100%	Research and Brainstorming	10 days	Wed 8/2/06	Tue 8/29/06	107			
110		100%	Prototyping or Refactoring	12 days	Wed 8/30/06	Fri 9/15/06	109			
111		50%	Unit Test	5 days	Mon 9/18/06	Fri 9/22/06	110			
112		0%	Design	5 days	Mon 9/25/06	Fri 9/29/06	111			
113		0%	Life Cycle, Branding, Task Manager	20 days	Mon 10/2/06	Fri 10/27/06				
114		0%	Research and Brainstorming	5 days	Mon 10/2/06	Fri 10/6/06	112			
115		0%	Prototyping or Refactoring	5 days	Mon 10/9/06	Fri 10/13/06	114			
116		0%	Unit Test	5 days	Mon 10/16/06	Fri 10/20/06	115			
117		0%	Design	5 days	Mon 10/23/06	Fri 10/27/06	116			
118		0%	Harden (IDVT Prep)	5 days	Mon 10/30/06	Fri 11/3/06	117			
119		54%	Topology Perspective	79 days	Wed 7/5/06	Tue 10/24/06				
120		100%	Iteration 1	20 days	Wed 7/5/06	Tue 8/1/06				
125		75%	Iteration 2	23 days	Wed 8/2/06	Fri 9/1/06				
126		100%	Research and Brainstorming	5 days	Wed 8/2/06	Tue 8/8/06	124			
127		100%	Prototyping or Refactoring	5 days	Wed 8/9/06	Tue 8/15/06	126			


ID		% Comp	Task Name	Duration	Start	Finish	Predecessor	Qtr 1, 2006		
								Dec	Jan	Feb
128		100%	Unit Test	5 days	Wed 8/16/06	Fri 8/25/06	127			
129		0%	Design	5 days	Mon 8/28/06	Fri 9/1/06	128			
130		0%	Iteration 3	27 days	Mon 9/11/06	Tue 10/17/06				
131		0%	Research and Brainstorming	5 days	Mon 9/11/06	Tue 9/26/06	129			
132		0%	Prototyping or Refactoring	5 days	Wed 9/27/06	Tue 10/3/06	131			
133		0%	Unit Test	5 days	Wed 10/4/06	Tue 10/10/06	132			
134		0%	Design	5 days	Wed 10/11/06	Tue 10/17/06	133			
135		0%	Harden (IDVT Prep)	5 days	Wed 10/18/06	Tue 10/24/06	134			
136		67%	Report Designer/Viewer	82 days	Wed 7/5/06	Fri 10/27/06				
137		100%	Iteration 1	20 days	Wed 7/5/06	Tue 8/1/06				
142		100%	Iteration 2	24 days	Wed 8/2/06	Tue 9/5/06				
148		17%	Iteration 3	33 days	Wed 9/6/06	Fri 10/20/06				
149		50%	Research and Brainstorming	8 days	Wed 9/6/06	Fri 9/15/06	147			
150		0%	Prototyping or Refactoring	5 days	Mon 9/18/06	Fri 9/22/06	149			
151		0%	Unit Test	5 days	Mon 9/25/06	Fri 9/29/06	150			
152		0%	Design	5 days	Mon 10/16/06	Fri 10/20/06	151			
153		0%	Harden (IDVT Prep)	5 days	Mon 10/23/06	Fri 10/27/06	152			
154		0%	Data Collection/Agent Admin Perspective	77 days	Wed 10/25/06	Tue 2/13/07				
171		0%	Server Administration Perspective	65 days	Mon 11/6/06	Wed 2/7/07				
188		0%	Alert Viewer/Editor Perspective	78 days	Mon 10/30/06	Mon 2/19/07				
205		5%	Phase 2 code - Other	257 days?	Thu 1/26/06	Tue 1/30/07				
206		0%	IRA for Omegamon	20 days	Thu 1/26/06	Wed 2/22/06				
207		0%	Design	5 days	Thu 1/26/06	Wed 2/1/06				
208		0%	Code	15 days	Thu 2/2/06	Wed 2/22/06	207			
209		0%	CBE/WEF event generation	30 days	Wed 10/11/06	Tue 11/21/06				
210		0%	Design	15 days	Wed 10/11/06	Tue 10/31/06	37			
211		0%	Code	15 days	Wed 11/1/06	Tue 11/21/06	210			
212		0%	Port bugs to Bugzilla	5 days	Wed 9/27/06	Tue 10/3/06				
213		0%	Port tracks from 3.2	5 days	Thu 11/2/06	Wed 11/8/06	246SS			
214		0%	SMI-S certification (for some profiles)	1 day?	Thu 1/26/06	Thu 1/26/06				
215		5%	SMI CTP testing/Plugfest Participation	70 days	Wed 9/13/06	Tue 1/30/07	4			
216		41%	Eclipse Summit preparation	4 days	Mon 9/18/06	Thu 9/21/06				





ID	%	Comp	Task Name	Duration	Start	Finish	Predecess	Qtr 1, 2006		
								Dec	Jan	Feb
217		30%	Poster Session preparation	3 days	Mon 9/18/06	Wed 9/20/06				
218		50%	Presentation preparation	4 days	Mon 9/18/06	Thu 9/21/06	217SS			
219										
220		0%	Phase 2 Documentation	279 days	Thu 1/26/06	Thu 3/1/07				
221		0%	Incubation 0.2	8 days	Wed 12/6/06	Fri 12/15/06				
222		0%	Release Notes	8 days	Wed 12/6/06	Fri 12/15/06	224			
223		0%	Incubation 0.3	66 days	Wed 11/29/06	Thu 3/1/07				
224		0%	Online Help (Javahelp)	5 days	Wed 11/29/06	Tue 12/5/06				
225		0%	Online Help (Eclipse)	20 days	Mon 12/18/06	Mon 1/15/07	222			
226		0%	User's Guide	5 days	Tue 2/6/07	Mon 2/12/07	235			
227		0%	Release Notes	8 days	Tue 2/13/07	Thu 2/22/07	226			
228		0%	Installation Guide	5 days	Fri 2/23/07	Thu 3/1/07	227			
229		0%	API Manual/Programmer's Guide Documentation	261 days	Thu 1/26/06	Mon 2/5/07				
230		0%	Agent	20 days	Mon 10/2/06	Fri 10/27/06	32			
231		0%	Device Server	20 days	Mon 12/18/06	Mon 1/15/07	40			
232		0%	Database	20 days	Tue 11/14/06	Wed 12/13/06	74			
233		0%	Data Server	20 days	Mon 11/13/06	Fri 1/12/07	77			
234		0%	GUI	5 days	Thu 1/26/06	Wed 2/1/06				
235		0%	Editing, cleanup, etc.	15 days	Tue 1/16/07	Mon 2/5/07	230,231,232			
236										
237		2%	Phase 2 Test	145 days	Mon 8/7/06	Thu 3/1/07				
238		4%	Test Preparation	121 days	Mon 8/7/06	Fri 1/26/07				
239		20%	Test Plan/Planning	25 days	Mon 8/7/06	Fri 9/22/06	3			
240		0%	Write Plan	8 days	Mon 9/25/06	Wed 10/4/06	239			
241		0%	Hold Review	7 days	Thu 10/5/06	Fri 10/13/06	240			
242		0%	Create/Migrate Scenarios/Testcases	15 days	Mon 10/16/06	Fri 11/3/06	241			
243		0%	Create GUI testases	62 days	Mon 10/30/06	Fri 1/26/07	136			
244		0%	Set up Environment	5 days	Thu 10/26/06	Wed 11/1/06	96			
245		0%	Run Test	83 days	Thu 11/2/06	Thu 3/1/07				
246		0%	Execute Test - v0.2	34 days	Thu 11/2/06	Thu 12/21/06	244			
247		0%	Execute Test - v0.3	49 days	Fri 12/22/06	Thu 3/1/07	246			
248		0%	Support Test	83 days	Thu 11/2/06	Thu 3/1/07	246SS			


ID		% Comp	Task Name	Duration	Start	Finish	Predecessor	Qtr 1, 2006		
								Dec	Jan	Feb
249		0%	v0.2 Availability	1 day	Fri 12/22/06	Fri 12/22/06	246			
250		0%	v0.3 Availability	1 day	Fri 3/2/07	Fri 3/2/07	247			
251										
252		5%	Eclipse Incubation tasks	324 days	Fri 6/23/06	Thu 9/27/07				
253		0%	Identify critical Use Cases	11 days	Thu 9/14/06	Thu 9/28/06				
254		100%	Gather Initial Code Contributions	0 days	Fri 6/23/06	Fri 6/23/06				
255		100%	Fill out one or more Code Contribution Questionnaires	0 days	Fri 6/23/06	Fri 6/23/06				
256		75%	Create a High Level Phase II Design	35 days	Fri 8/4/06	Fri 9/22/06				
257		100%	Create Prototype	0 days	Fri 9/15/06	Fri 9/15/06	253SS			
258		0%	Create and maintain a Project Plan & Schedule	5 days	Thu 9/14/06	Wed 9/20/06	253SS			
259		100%	Capture Bugzilla usage process	1 day	Thu 9/14/06	Thu 9/14/06	253SS			
260		25%	Acquire the necessary rights to all required intellectual proper	24 days	Fri 8/25/06	Thu 9/28/06				
261		0%	Create and maintain a Project Log	10 days	Thu 9/14/06	Thu 9/28/06	253SS			
262		0%	Create and maintain a Project Status page	10 days	Thu 9/14/06	Wed 9/27/06	253SS			
263		85%	Hold API design and specification reviews	0 days	Wed 10/11/06	Wed 10/11/06	2			
264		0%	Recommend (start) nightly heartbeat builds	1 day	Fri 9/29/06	Fri 9/29/06	261			
265		0%	Eclipse Legal Review	34 days	Thu 9/14/06	Tue 10/31/06				
266		0%	Initial contribution	12 days	Thu 9/14/06	Fri 9/29/06	253SS			
267		0%	Third party components	34 days	Thu 9/14/06	Tue 10/31/06	253SS			
268		0%	Develop Community of Committers	0 days	Tue 10/31/06	Tue 10/31/06				
269		0%	Develop Community of Users	0 days	Tue 10/31/06	Tue 10/31/06				
270		0%	Develop Community of Plug-in Developers	0 days	Tue 10/31/06	Tue 10/31/06				
271		0%	Release 1 Preparation	170 days	Tue 10/31/06	Fri 6/29/07				
272		0%	Readiness Checkpoint	0 days	Tue 10/31/06	Tue 10/31/06				
273		0%	Readiness Checkpoint	0 days	Fri 3/30/07	Fri 3/30/07				
274		0%	Readiness Checkpoint	0 days	Fri 6/29/07	Fri 6/29/07				
275		0%	Project Lead authors initial Release Review slides (PDF is pre	85 days	Fri 6/1/07	Thu 9/27/07				
276		0%	Proposers ask EMO to schedule an initial Release Review	85 days	Fri 6/1/07	Thu 9/27/07				
277		0%	EMO schedules an initial Release Review and announces it c	85 days	Fri 6/1/07	Thu 9/27/07				
278		0%	Post initial Release Review slides to project website and senc	85 days	Fri 6/1/07	Thu 9/27/07				
279		0%	Proposed Project Lead presents to the initial Release Review	85 days	Fri 6/1/07	Thu 9/27/07				
280		0%	Email copy of the current version of initial Release Review slic	85 days	Fri 6/1/07	Thu 9/27/07				


ID		% Comp	Task Name	Duration	Start	Finish	Predecess	Qtr 1, 2006		
								Dec	Jan	Feb
281		0%	EMO archives initial Release Review slides	85 days	Fri 6/1/07	Thu 9/27/07				

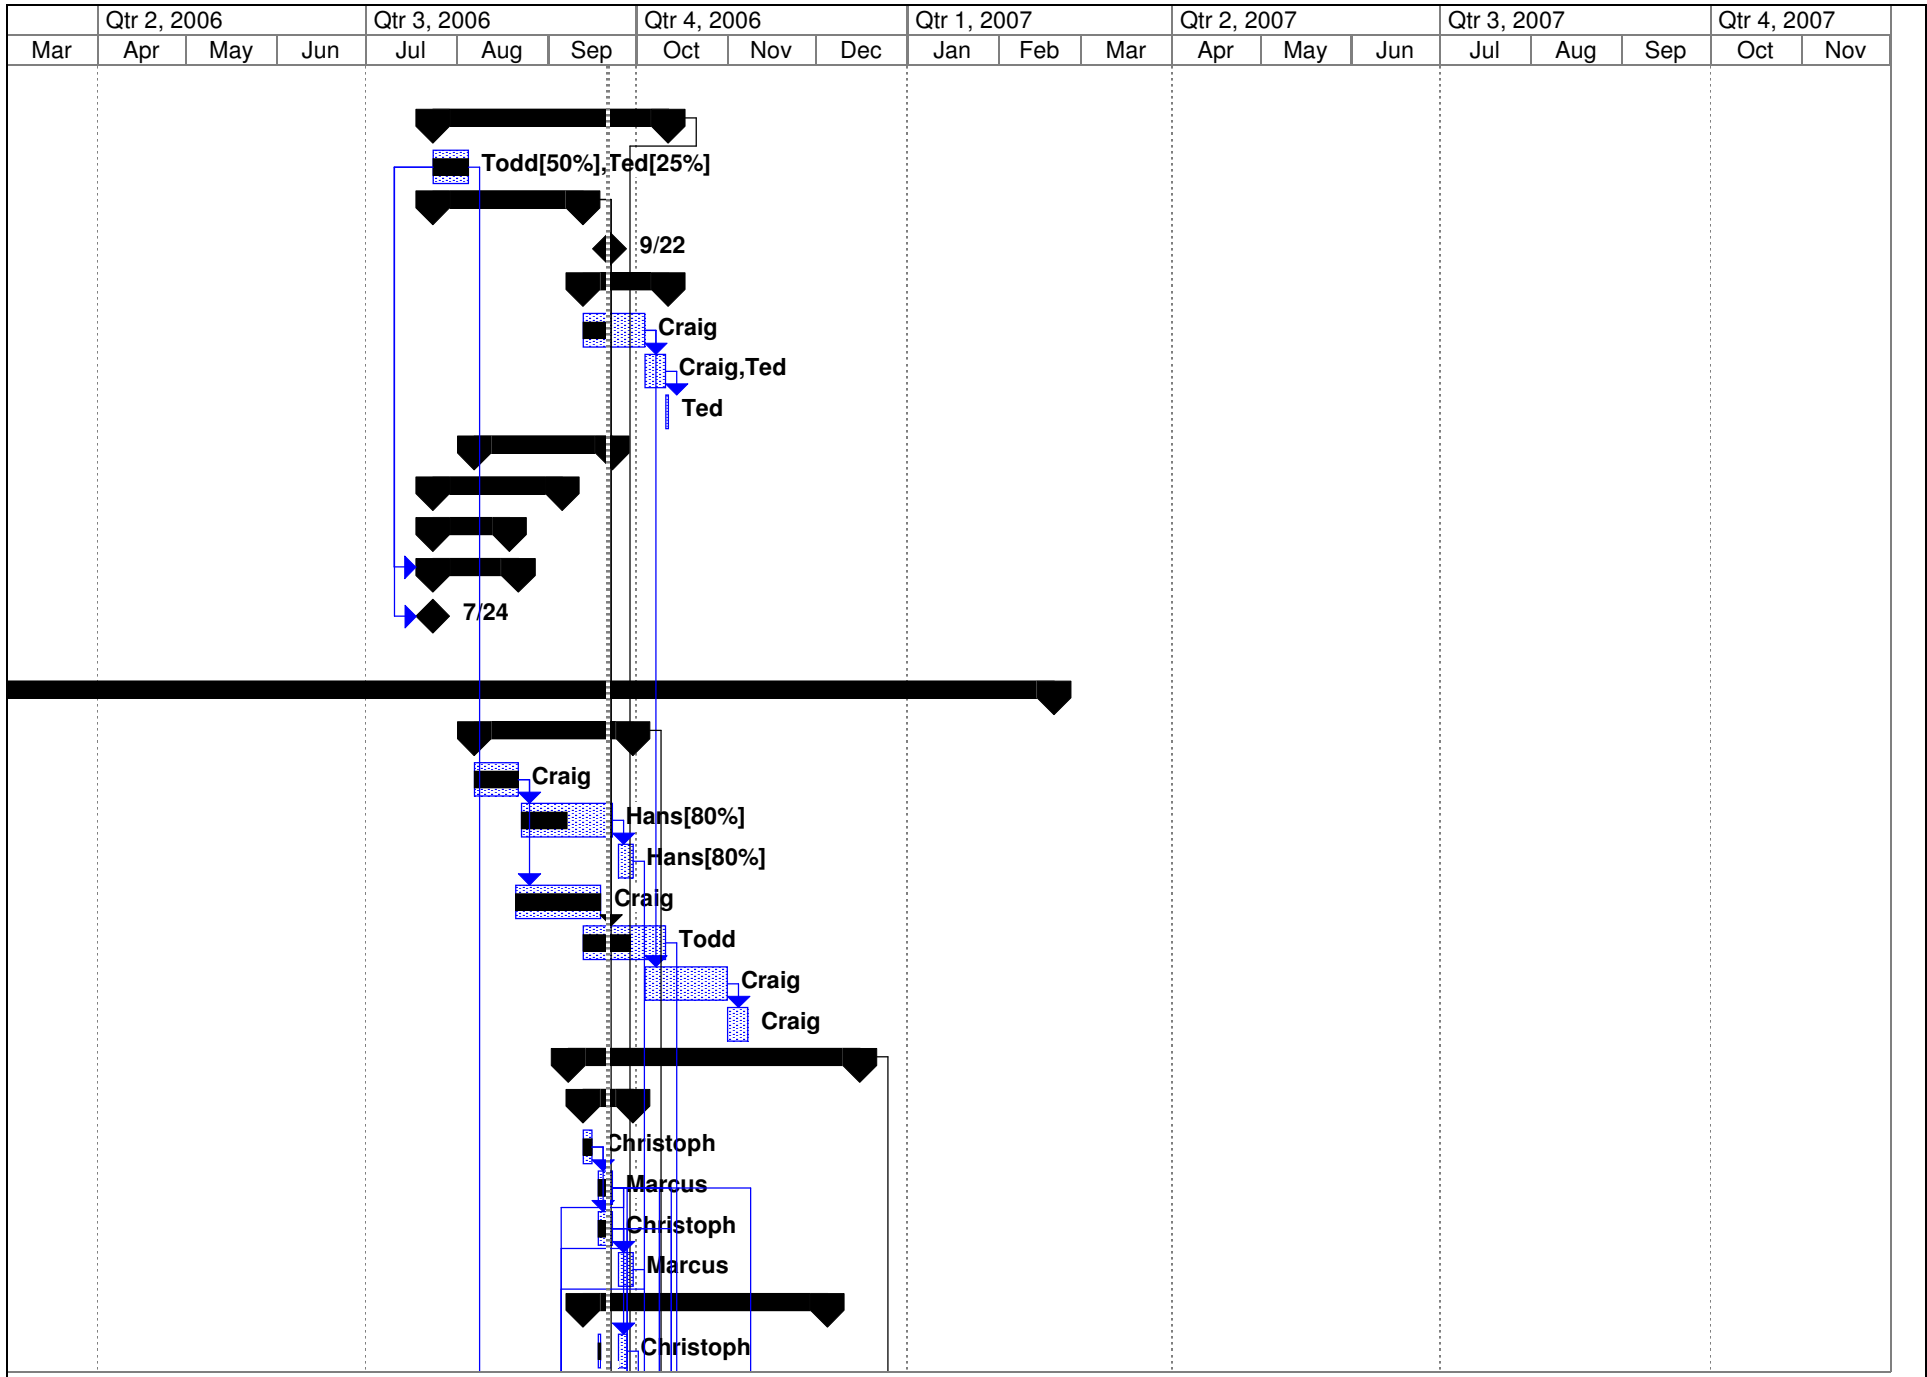

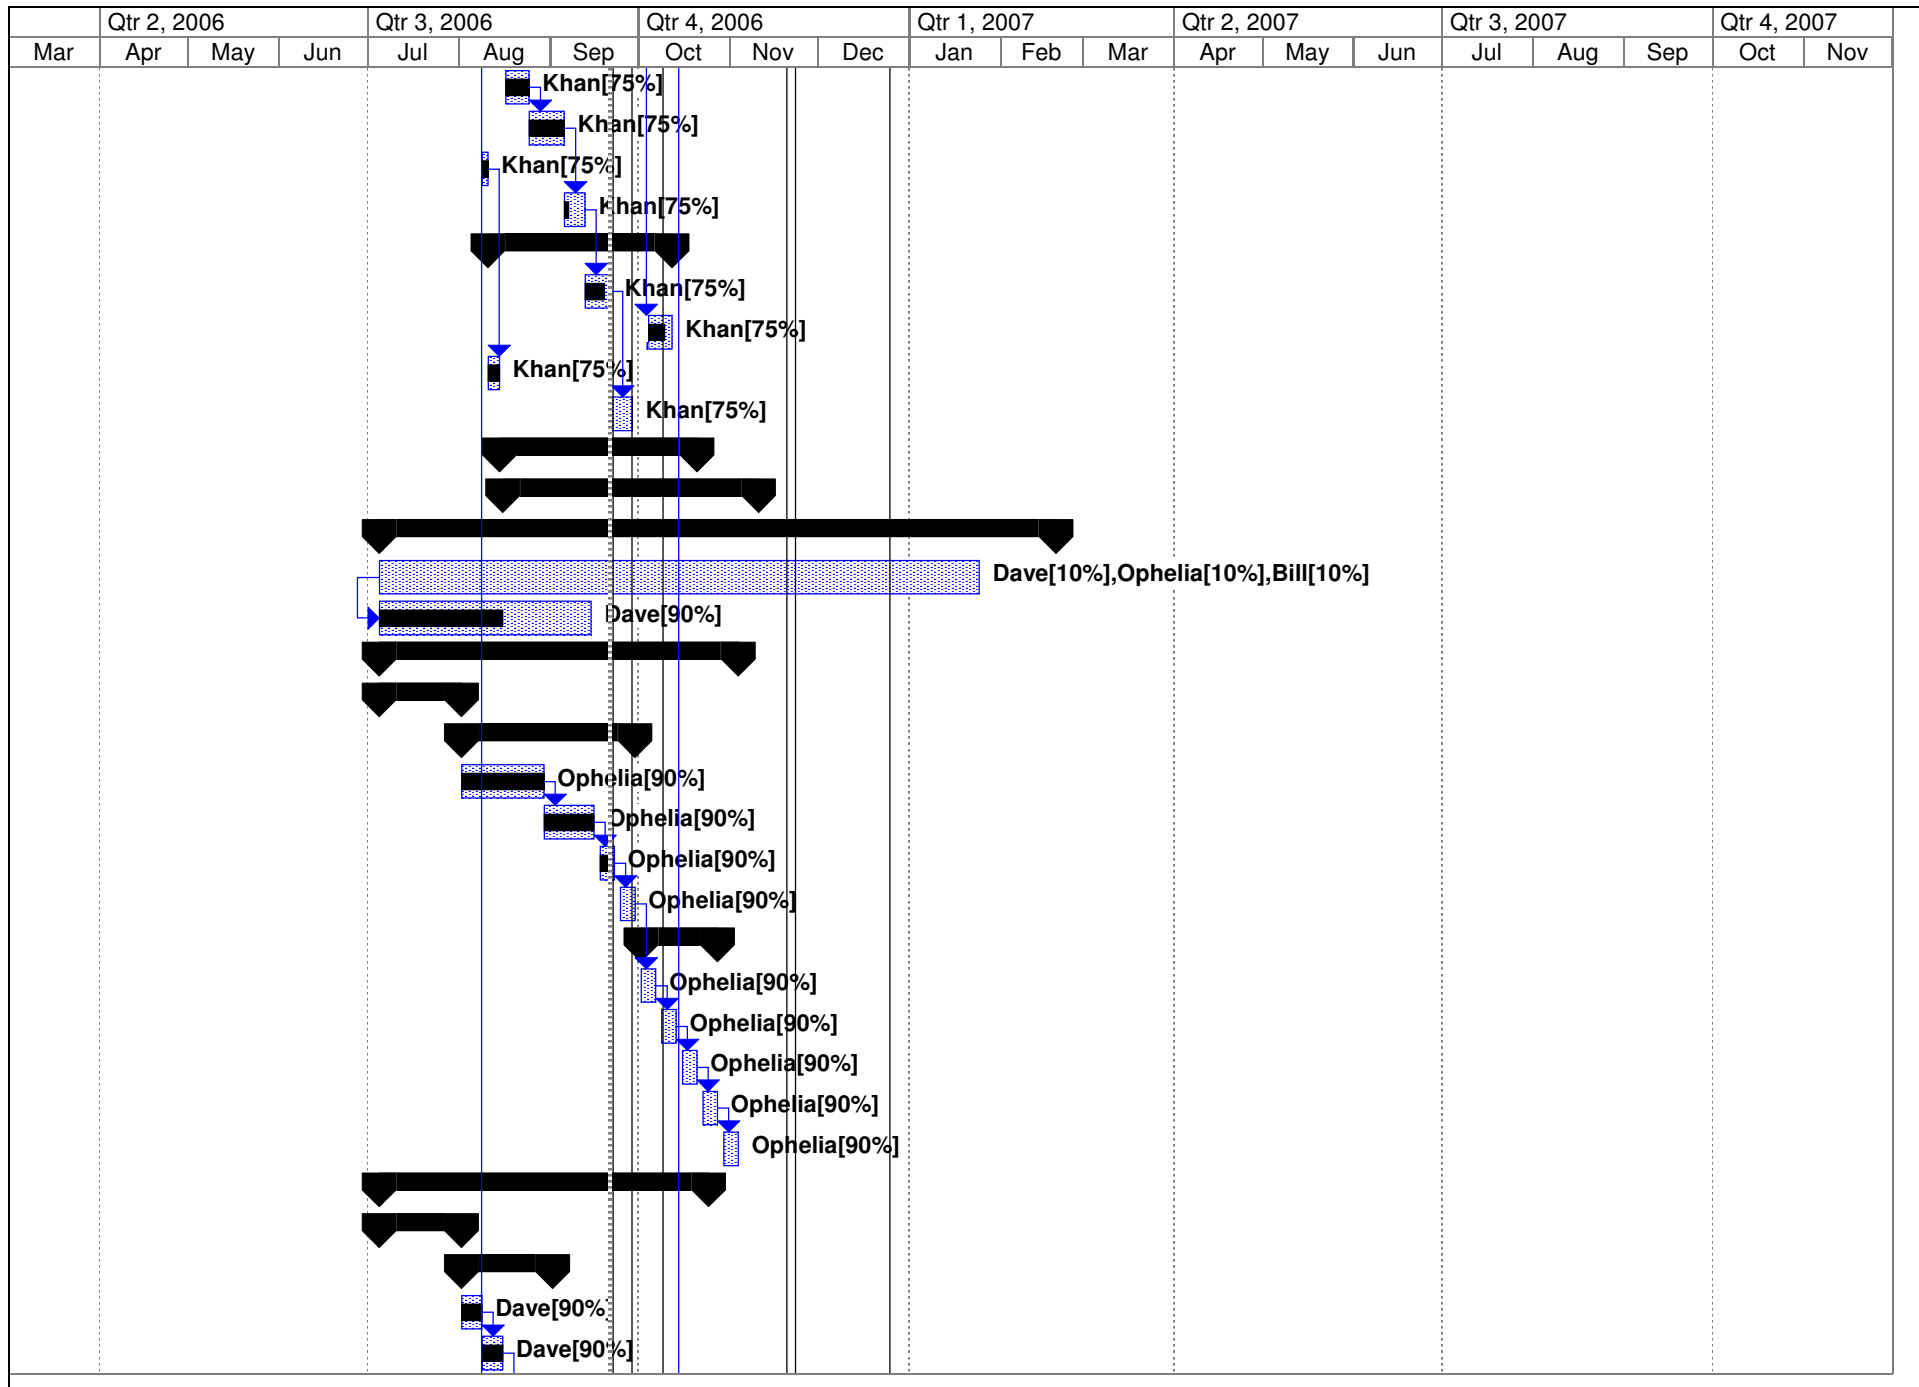

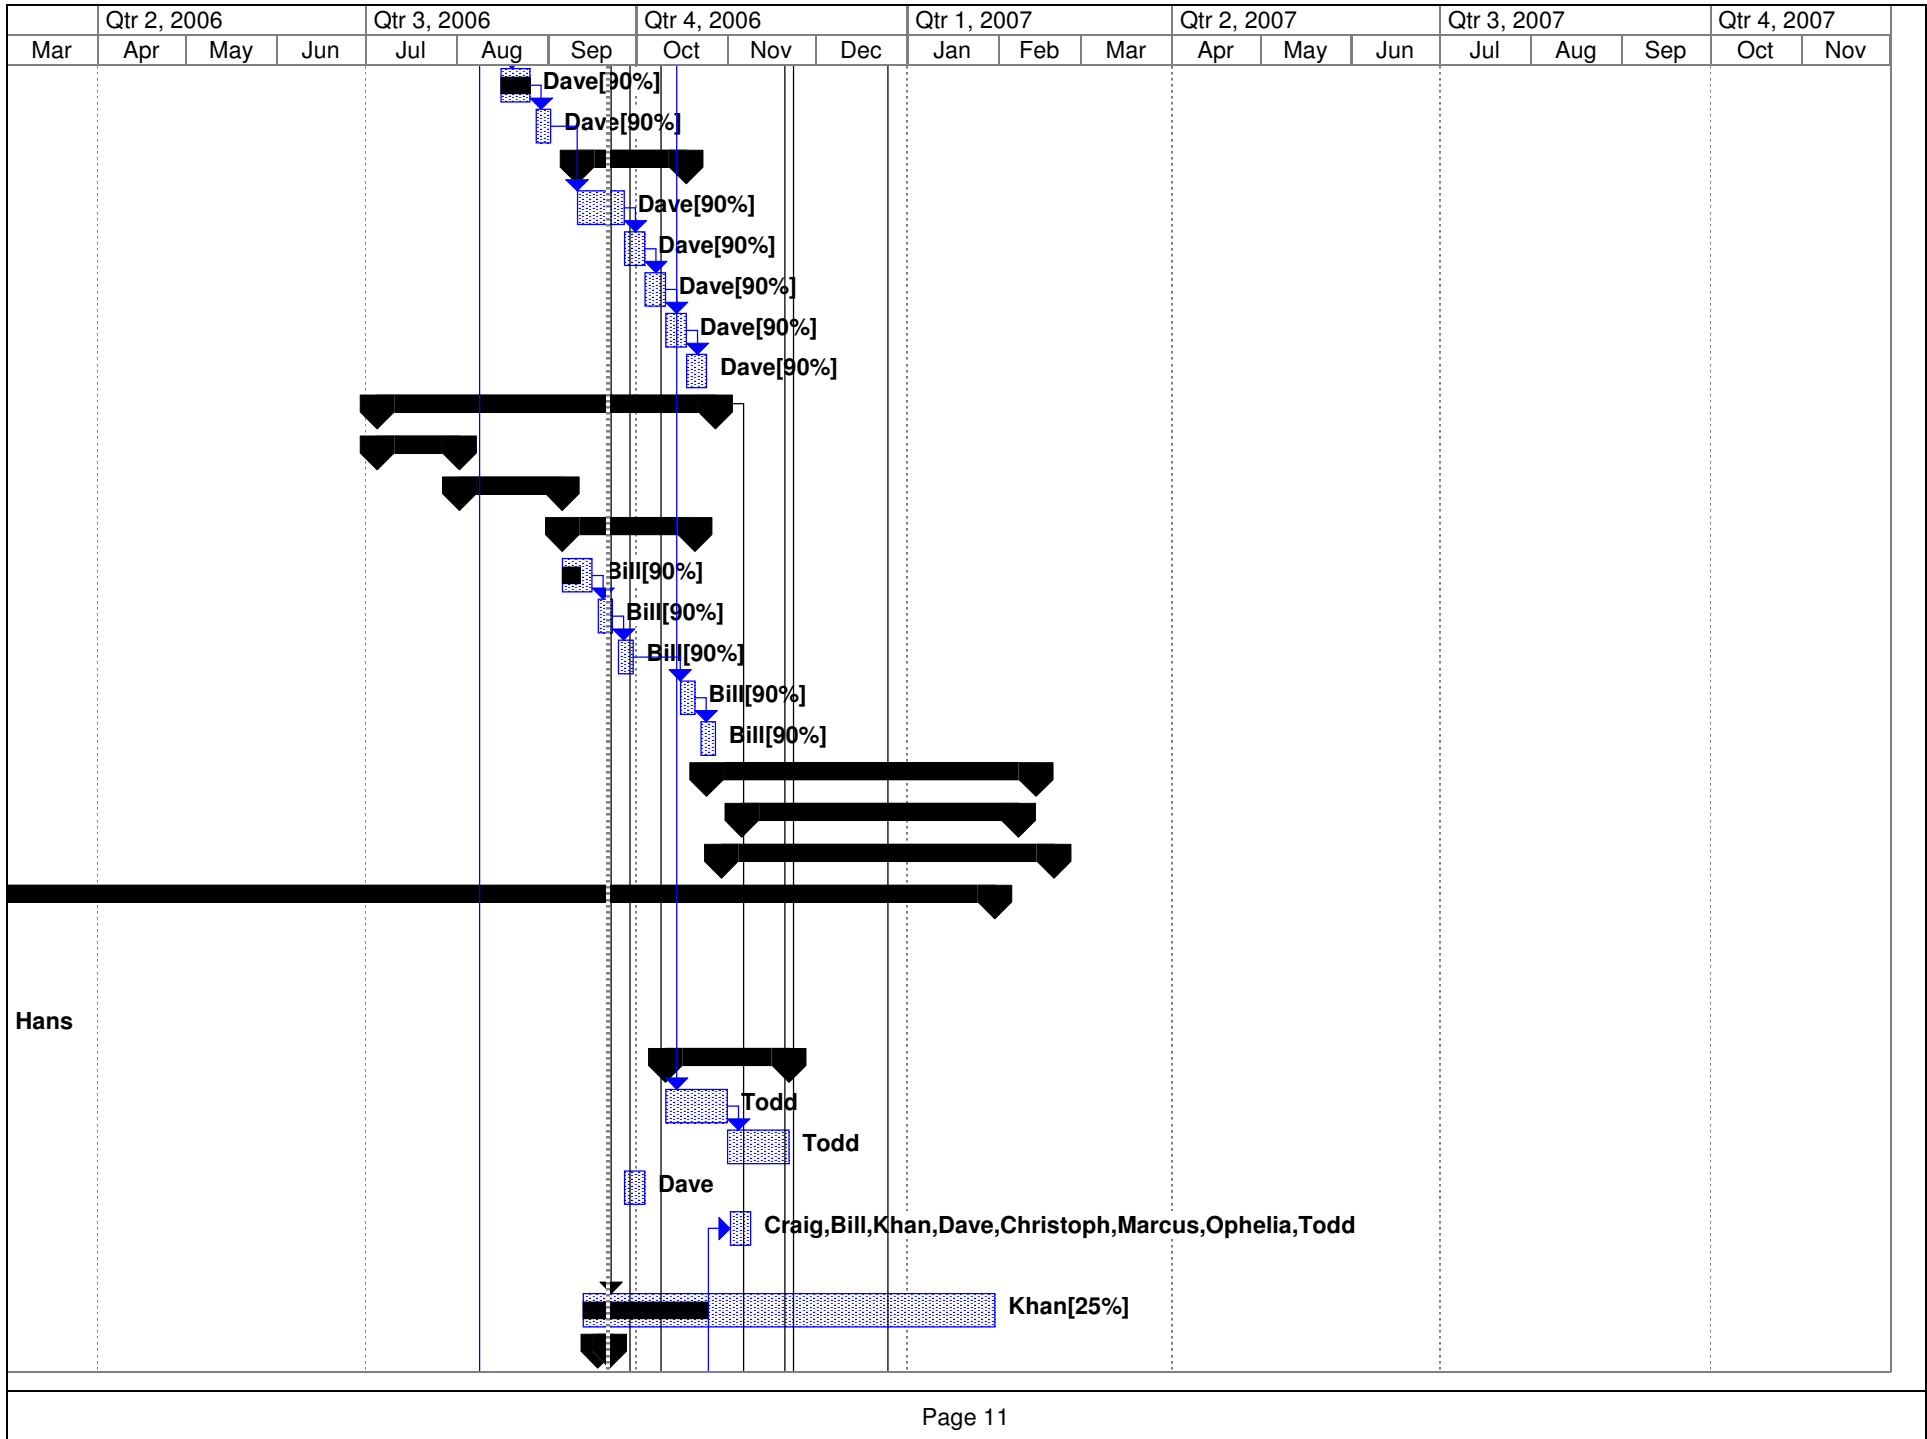

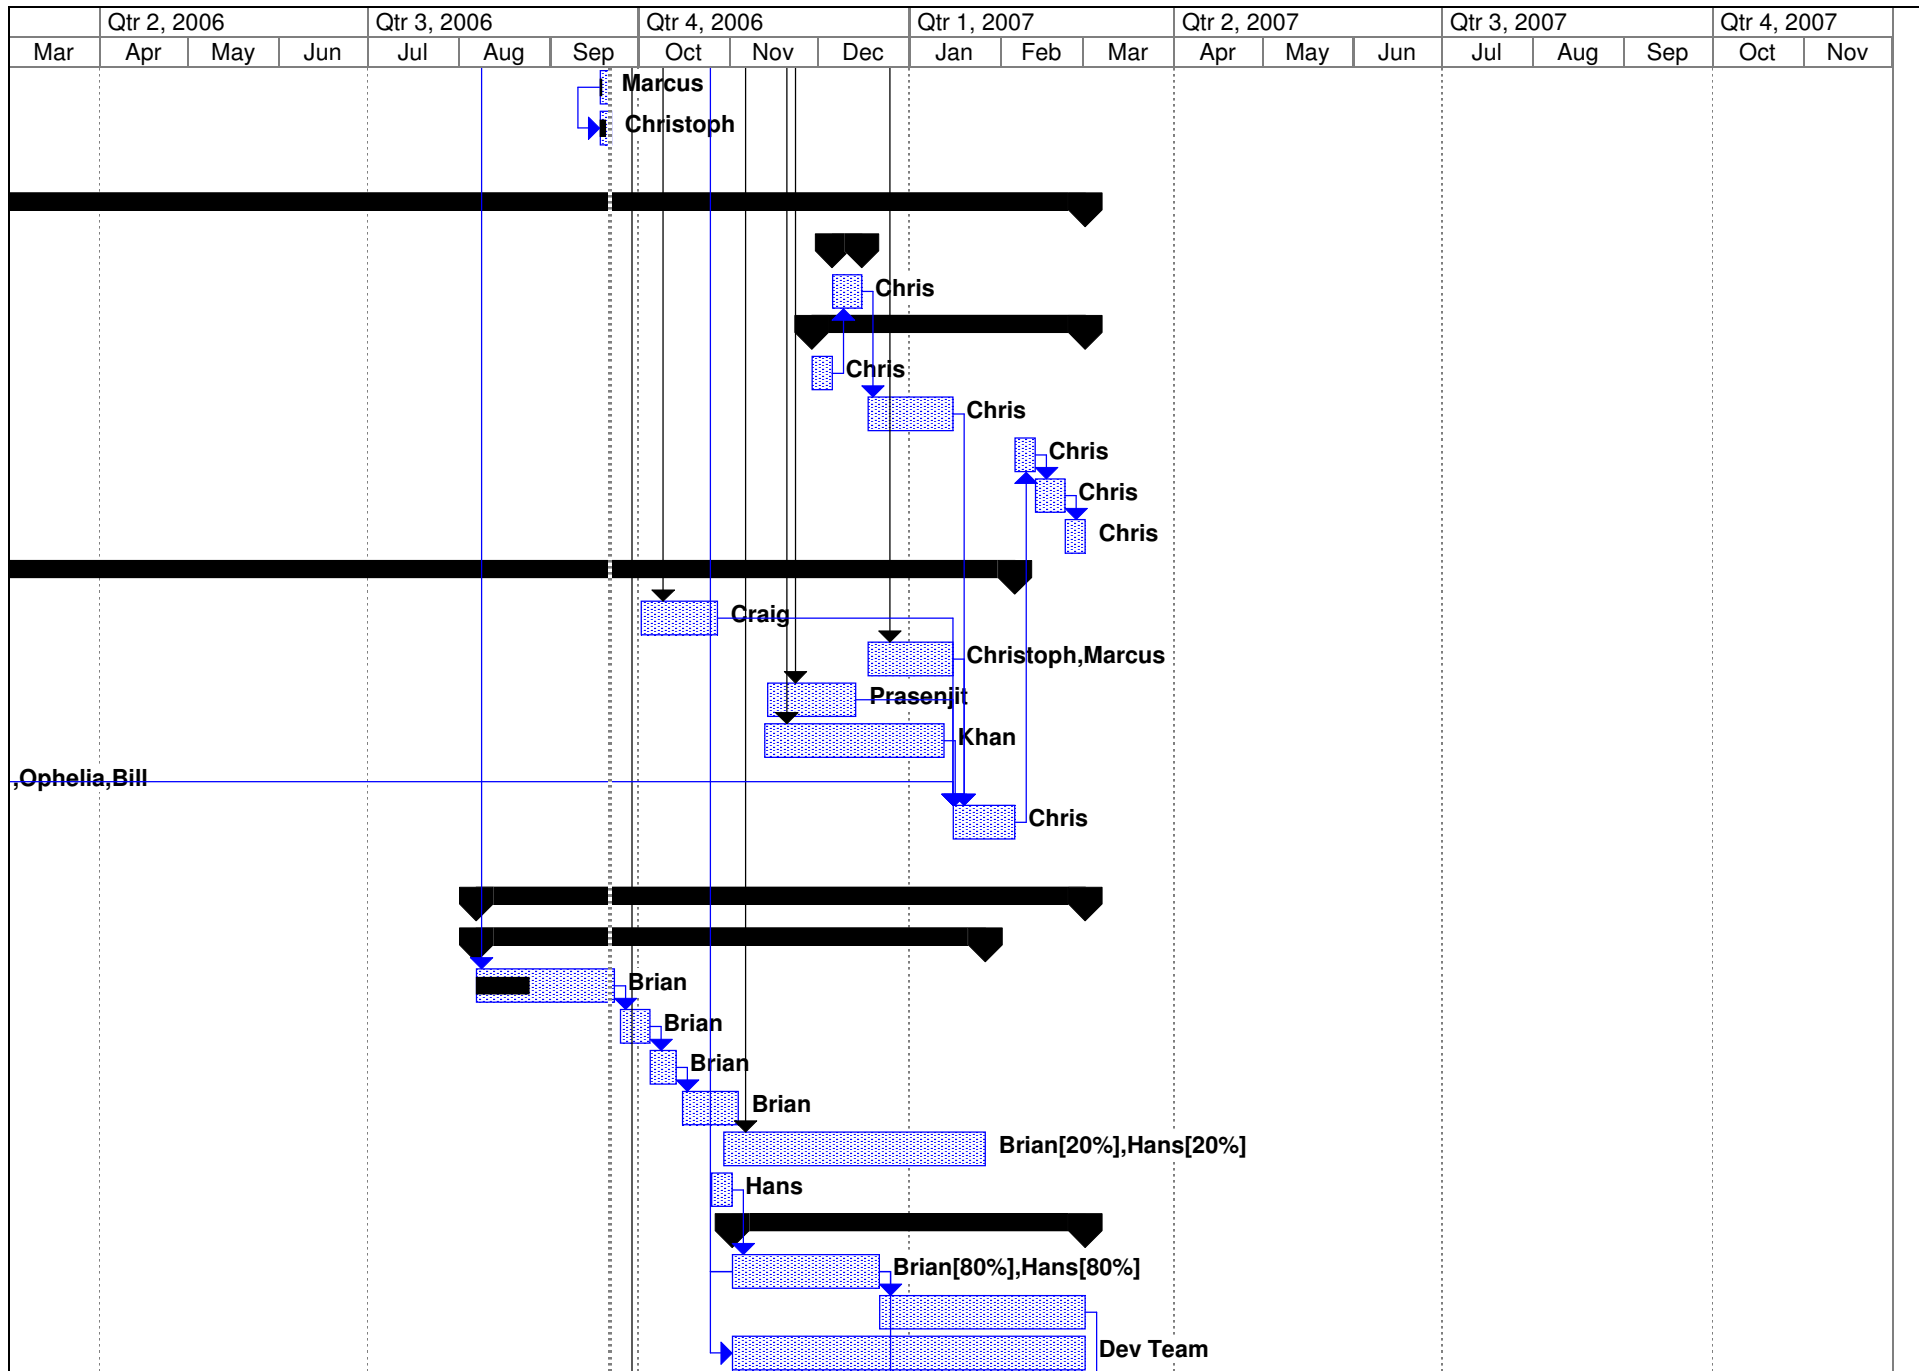

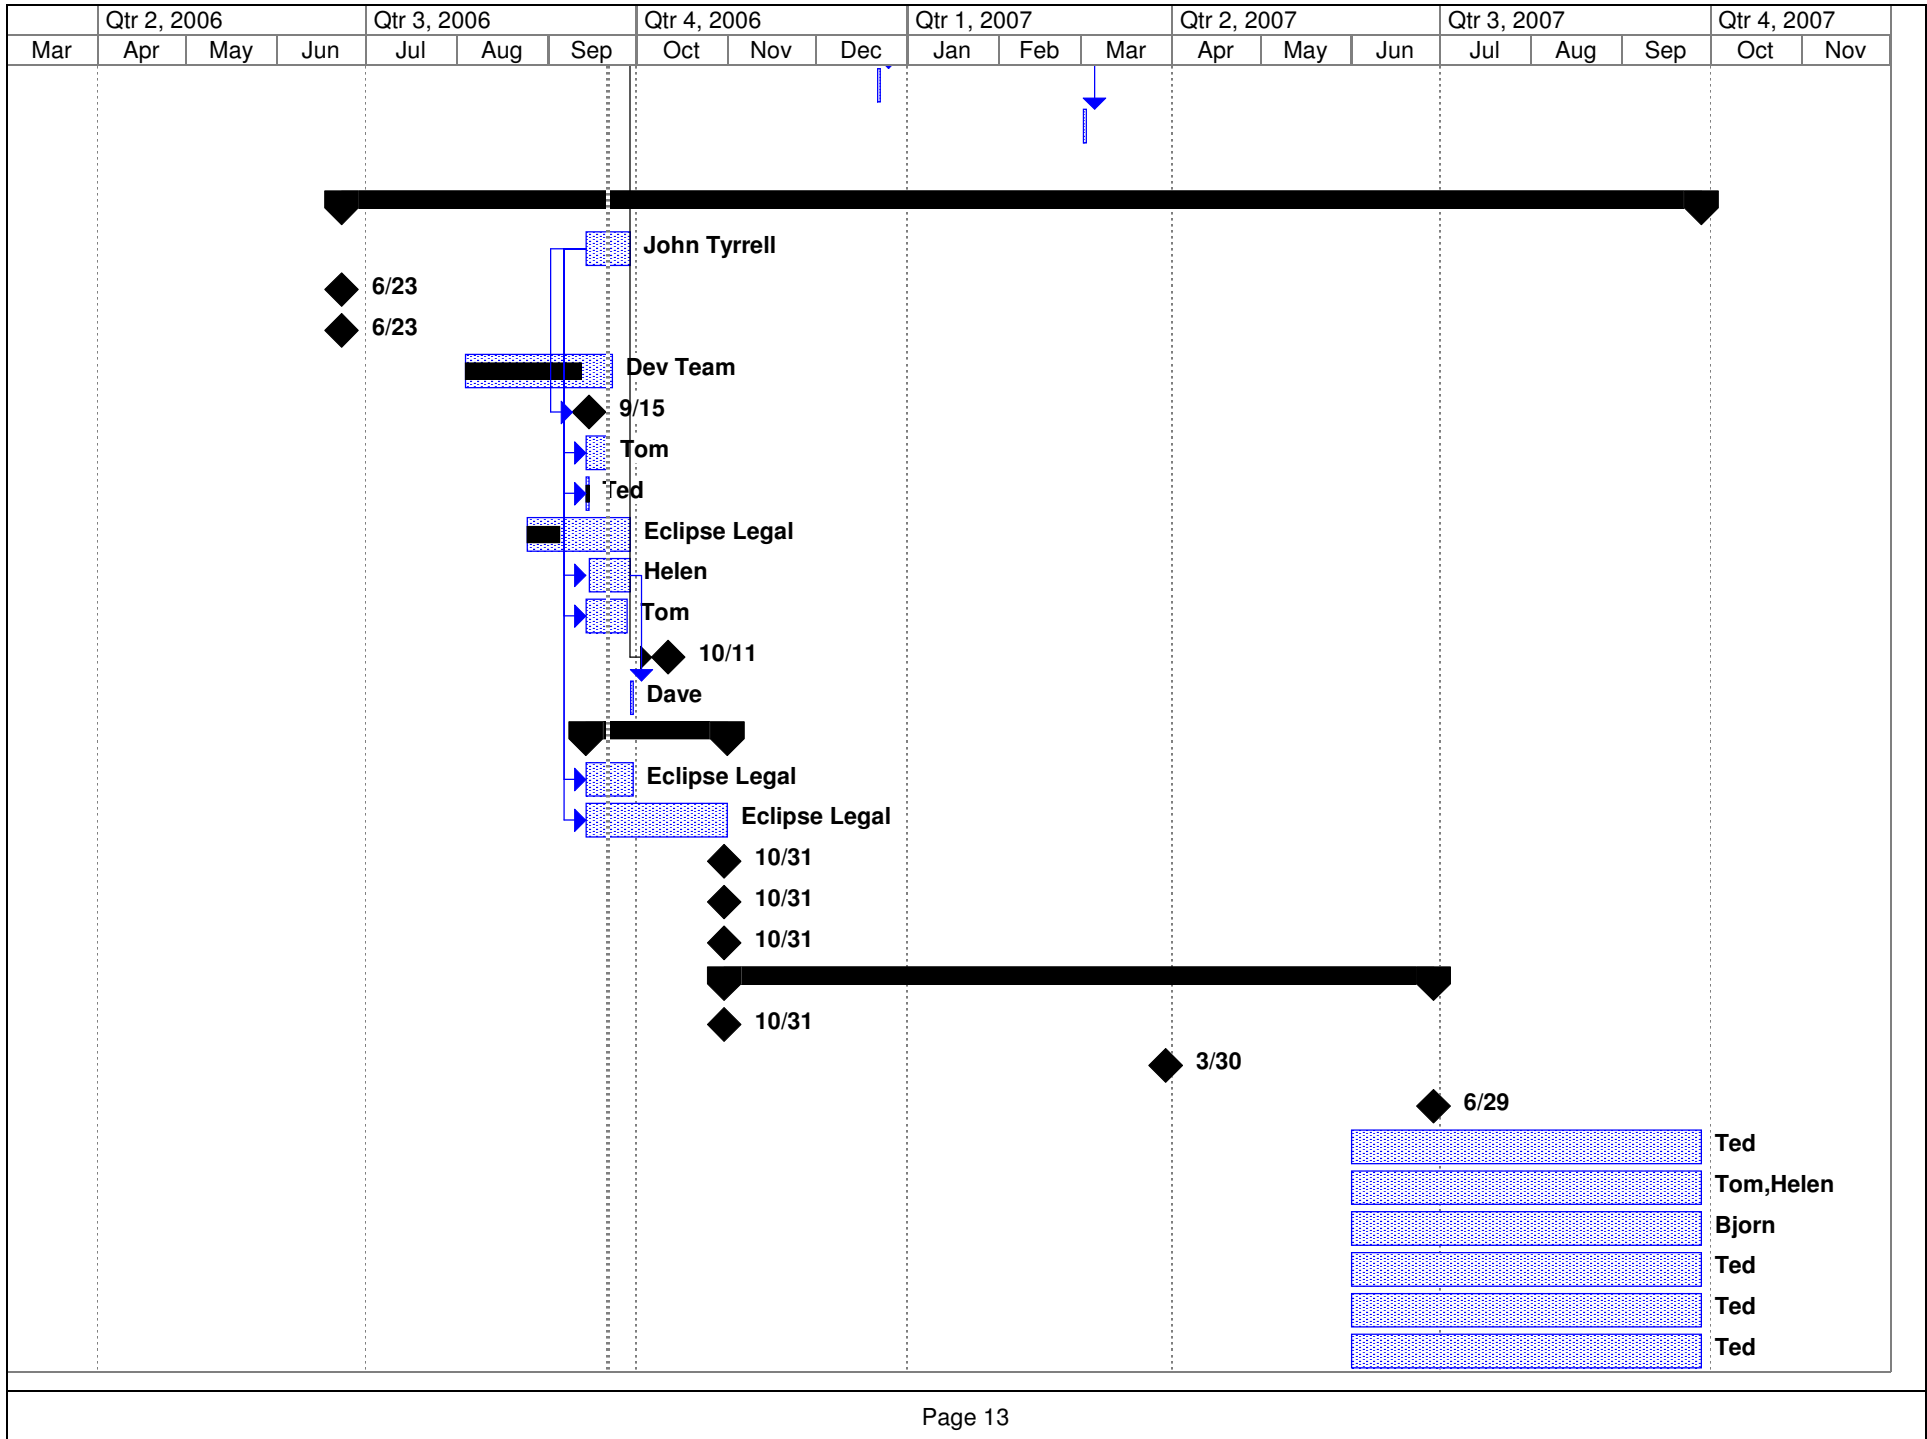

	Qtr 2, 2006				Qtr 3, 2006			Qtr 4, 2006			Qtr 1, 2007			Qtr 2, 2007			Qtr 3, 2007			Qtr 4, 2007	
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	
																					Bjorn
